


DC-Gun to Booster Transport Line Status



Gun side

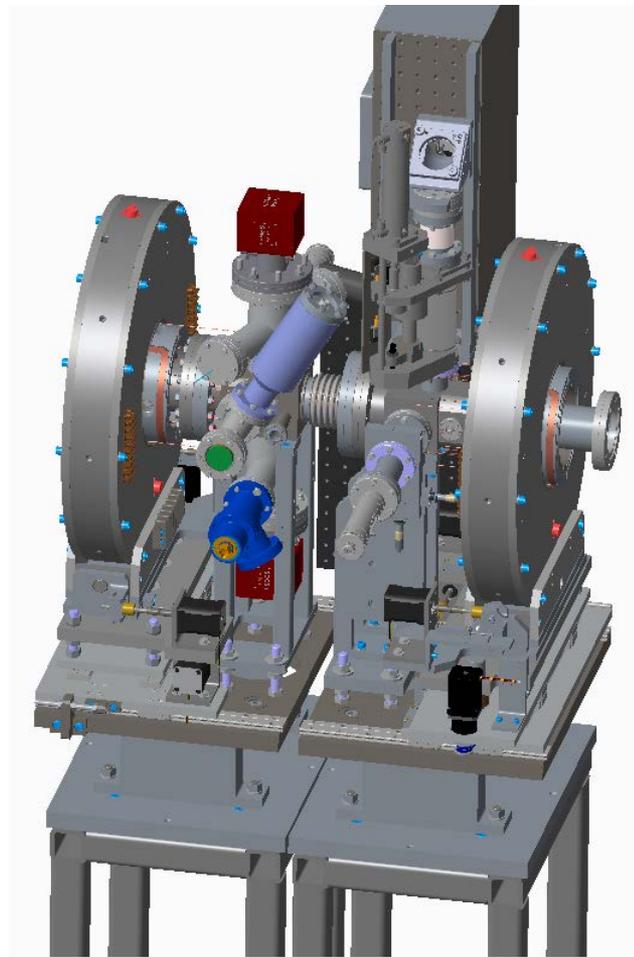

Booster side



Solenoid Magnet Assembly

- Some minor problems are fixed in the assembly.
- Axial load on one motor is putting too much force on armature, pulling the shaft a bit, so making necessary arrangement to fix that.

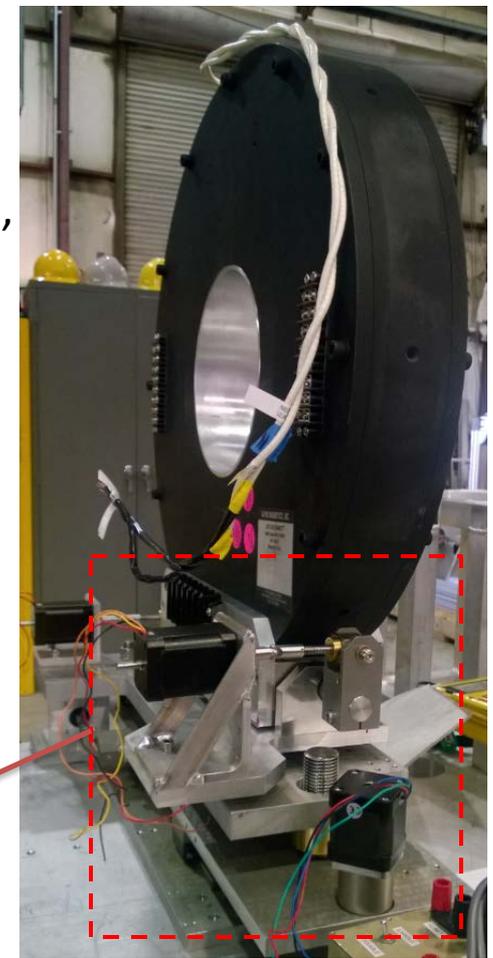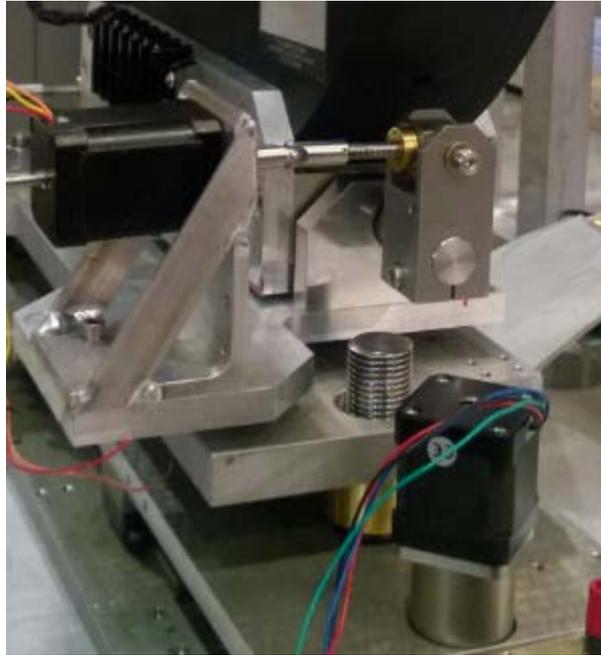

Vacuum Chambers

- One chamber is cleaned, baked and now is getting cleaned in clean room.
- Except four parts, I have everything for this assembly. The parts I need are YAG crystal holder, laser mirror and its holder and NEG pump can.
- Several parts going in the vacuum are being cleaned and baked.
- We could start assembling and testing this in the week of 19th Dec.
- Second vacuum chamber is getting baked now, would come out on Monday
- We should receive the third chamber today.

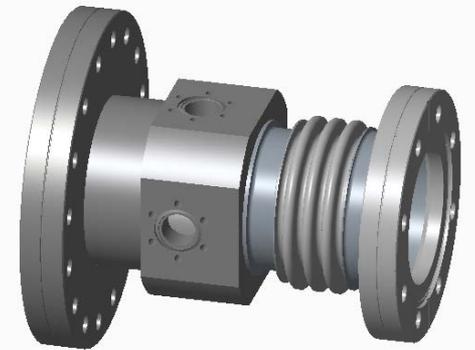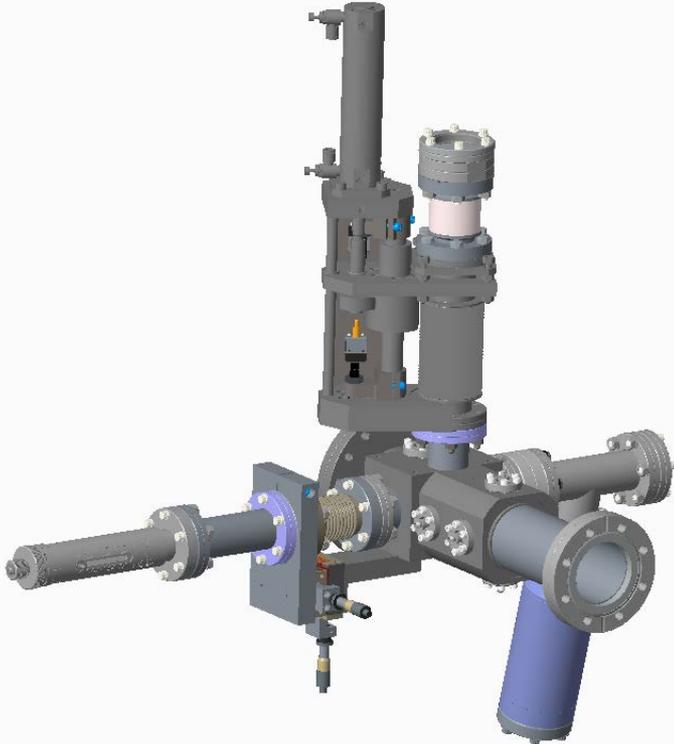

Installation Plan

- Floors are already marked and stands are ready to be installed.
- Delivery date of SS Laser mirrors is 16th Dec.
- Preliminary assembly and testing of all chambers would start in the 19th week of Dec, could go up to the 1st week of Jan.
- Final assembly in 2 O clock would be from 2nd week of Jan, would take about 3 weeks.

