




Accelerator Support and Maintenance



Run 14



Maintenance/Changeover Day

■ Major efforts RHIC:

- Access 0800-1300hrs.
- RA and CA in the tunnel.
- Polarity swap for BDH0 magnets.
- CeC installation all day (1500 sweep).
- Sweep 4 o'clock RF at 1300hrs.
- Ramp tests starting 1530.
- Setup with beam ~1800hrs.

■ Injectors remain on for development.

A vertical strip of four images on the left side of the slide. From top to bottom: a clock face on a blue background, a clock face on a yellow background, an open book on a green background, and an open book on a purple background.

Schedule

- 0730 Dump, download PASS code.
- Access to RHIC zone 2 promptly at 0800, all but kicker and RF areas.
- RHIC sweeps early afternoon in tunnel.
- Zone 2: Final tunnel sweep.
- Experiments can stay opened during ramp tests.



Time	Activity	Group
0730	Dump RHIC beam Run RHIC magnets to zero, remove I limit key. PASS Download	CAS/MCR/MSG
0800	RHIC tunnel Opened CA 4&12 o'clock XA 8 o'clock RA 2,6&10 o'clock Booster on for NSRL	MCR/MSG
1100	Sweep 5z1&6z2, 6 o'clock to XA	MSG/CAS/MCR
1500	Sweep 2 o'clock areas	MSG/CAS/MCR
1600	Begin ramp tests, then start setup	MSG/AP/MCR



- Details, plans and discussion here at 1430hrs



ACCELERATOR
ACCESS
Timetable

1600HRS




Ring Access
Complete



Access Key
 Restricted Access
 Controlled Access
 No Access

LINAC
LTB
Booster

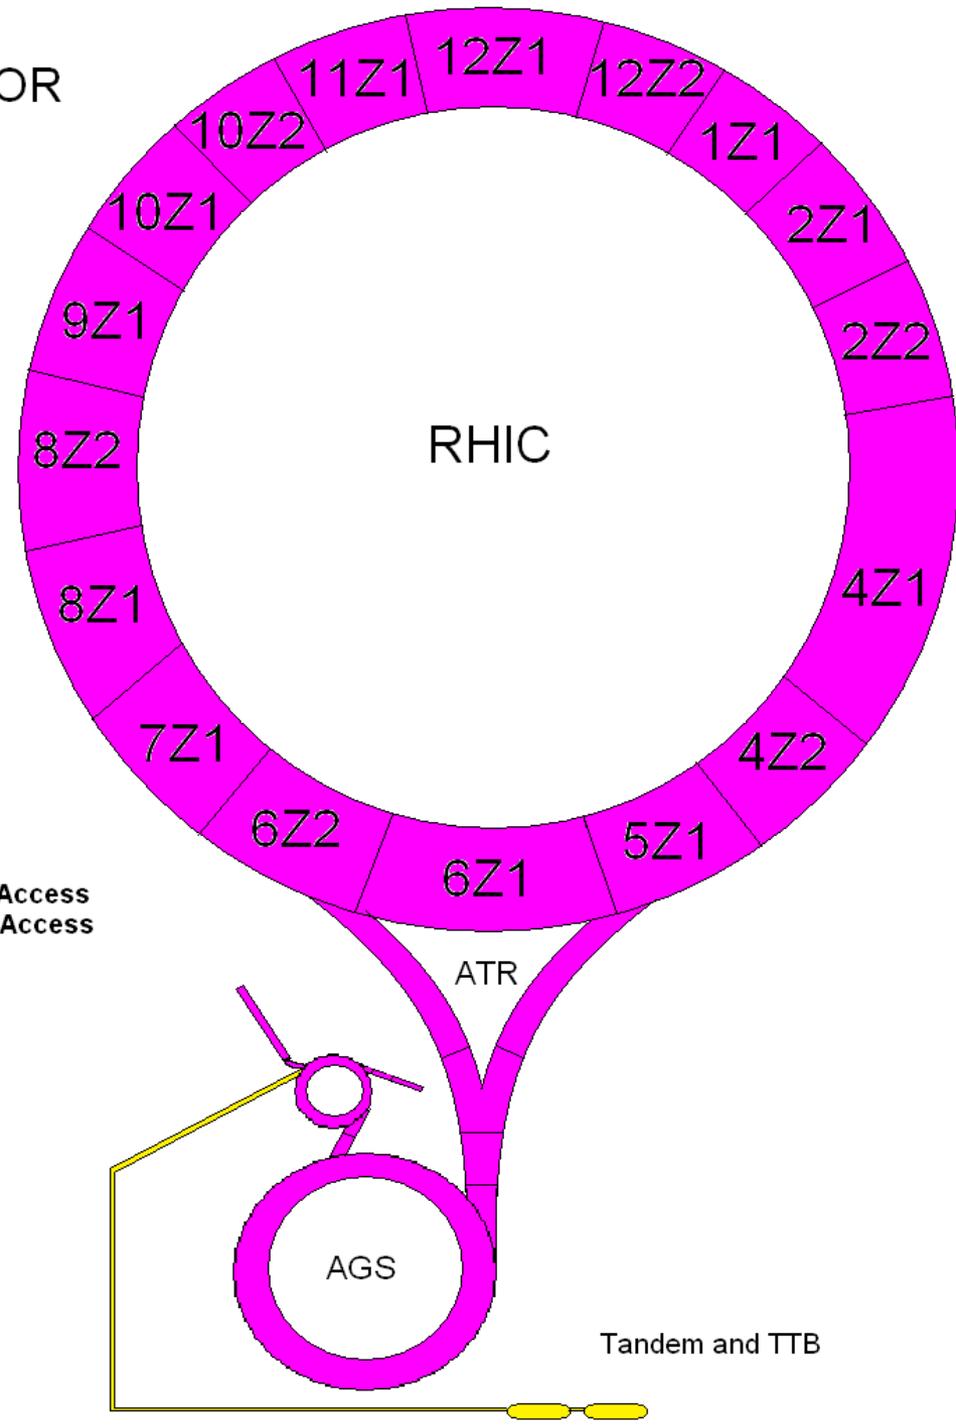

Tandem and TTB
