




Accelerator Support and Maintenance



Run 15

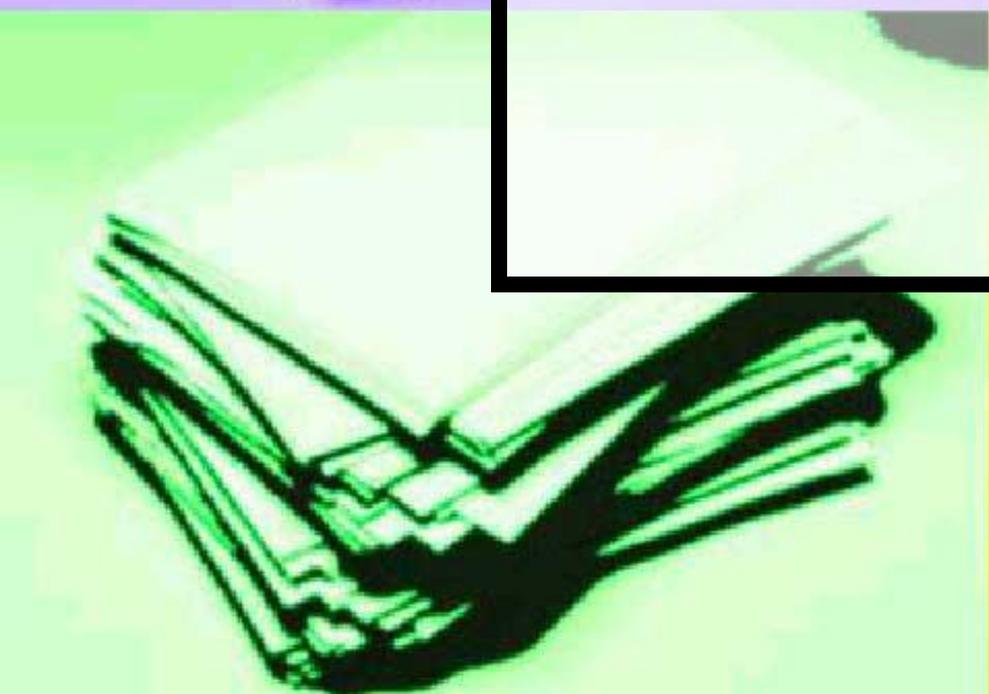

Scheduled Maintenance Tomorrow:



- Injectors down 0600-1500.
- RHIC down 0730-1600hrs.
- Some controlled Access.
- Sweeps of areas where work is complete start at 1300hrs.
- Approved work only...
- Details- Meeting here at 1430hrs

Schedule for Maintenance March 4th

Time	Activity	Personnel
0600	Siemens coast down Begin AGS and Booster CA LOTO	PSG MCR/CAS
0700	Begin Ramp down e-lens SC solenoids Begin Booster Access	MCR CAS/MSG
0730	Begin AGS Access Prepare to Dump RHIC beam	MCR/HP MCR
0800	STAR and PHENIX Opened after beam dump RA sector 2, 4, 6 after I<500 amps (Lim Key removed) Fence Adjacent to 2GE1 opened e-Lens warm element LOTO application CA to 9z1&10z2 for survey, sector 10 RA afterwards	MCR OC CAS MSG HP/MCR
1100	Booster and AGS Accesses complete, Remove LOTO Restore Booster when heater work complete Sweep 4z1 then RFNA- No access 56MHz conditioning	MCR/CAS MCR MCR
1300	Begin RHIC sweeps Restore AGS	CAS/MCR MCR
1500	Sweep all tunnel areas, IR 2 and 10 last RHIC Power supplies to injection	CAS/MCR RPSG
1600	Begin Hysteresis Ramp- Tunnel secured Sweep STAR and PHENIX	MCR/RPSG MCR/CAS
1700	Restore RHIC Physics	MCR/AP



ACCELERATOR
ACCESS
Timetable
1700hrs
Restore
Physics

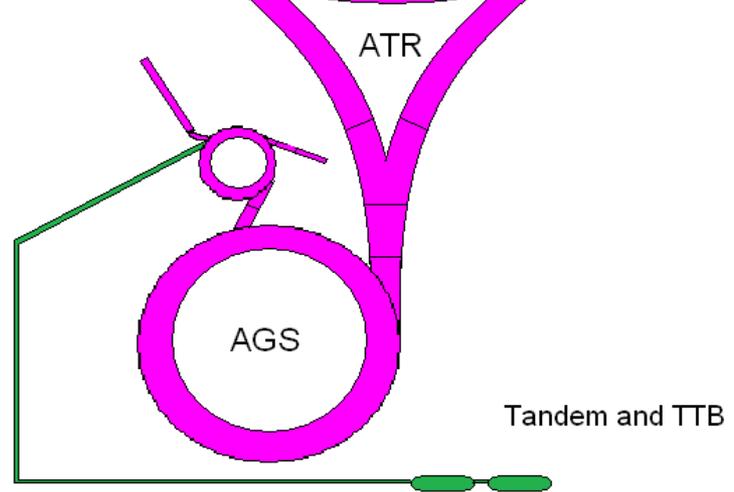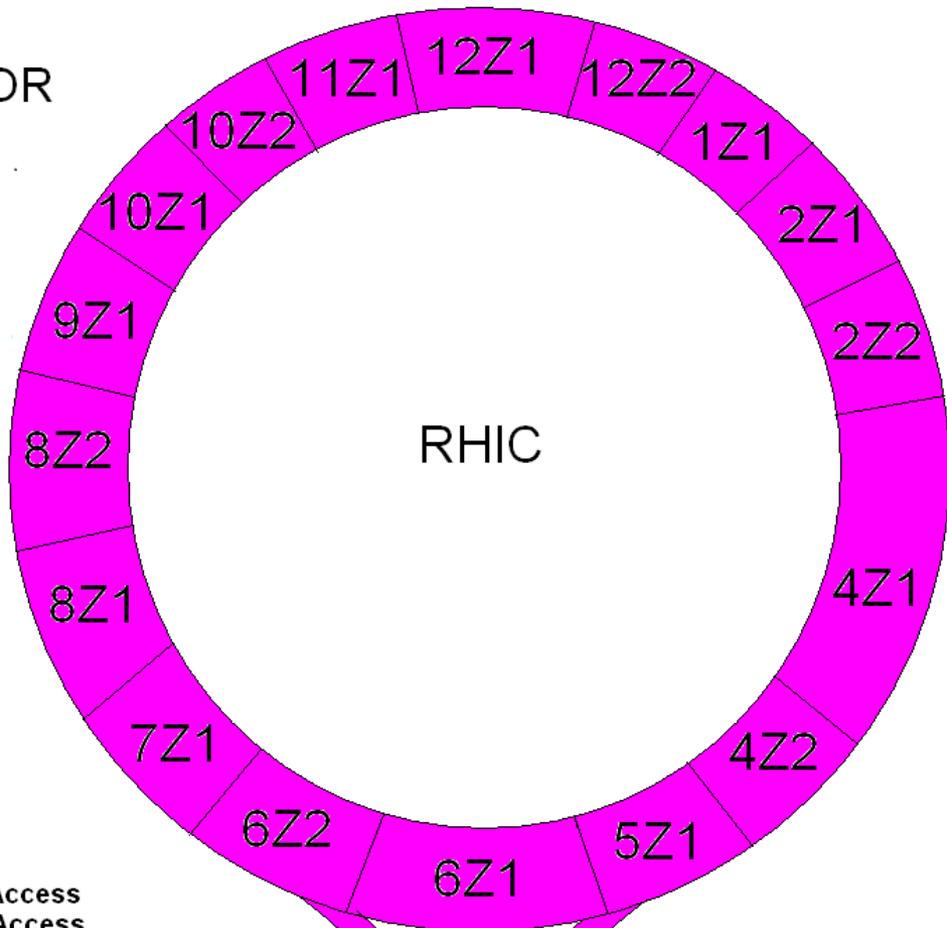

LINAC
LTB
Booster
