Minutes from Sector 1 Relocation Meeting, May 22nd 9:15 LCR

D. Gassner

- K Mernick suggest moving the BBQ kicker and triple purpose pick-up assemblies to sector 2, yellow (it appears that there is room). This allows shorter cable lengths, moving towards YO1 Q4 would have meant (undesirable) longer cables than the existing.
- K Mernick recommends that we don't need the moveable X-Y capability on the triple purpose pick-up, this can simplify the relocation effort and beam line assembly.
- K Mernick requests that the Quad PU (0.25m) from YO1 (40m) be relocated (instead of removed), a suggestion is closer to Q4 in YO1, get confirmation from Kevin on new location.
- Can remove the stochastic cooling ceramic pick-ups [6-9 GHz] in sector 2 yellow (62-66m from IP2) since these are no longer used, this makes more room for the first note mentioned above.
- The preference is for the IPMs to be installed as close to Q3 as possible in sector 12. Since they need to be offset because the beam pipes are close together, the horizontal should be closer to Q3. Jesse will layout new IPM locations (plan view) with longitudinal offset and separate stands for review.
- George suggests prioritizing the order of the installations and a bake-out schedule, see next comment.
- Need to get Mike Mapes & Dan Weiss involved as soon as possible for vacuum, mechanical and bake-out planning.
- Rob M is following up with Angelika regarding beta function considerations of the new proposed locations of the ARTUS kickers adjacent to the existing ones in sector 2.
- Confirmation that GOF magnets will stay in sector 1 (near Q3), need to check with Gary W's latest LEReC layout.
- Joe T says we can have designer Vito committed for this priority and need dedicated mechanical engineers.
- System Champions need to approve the relocation plan for their respective systems.
- Warm Space Committee needs to approve the relocation plan.

- **Note: the following slides from the meeting have not been updated to include the above comments made during the meeting.**

Sector 1 Instrument Relocation for LEReC

About 25m of RHIC transport (from 39-64m from IP2) needs to be cleared out soon after Run15 ends so the LEReC beam lines can be installed.

LEReC Phase-I layout: cooling sections in RHIC

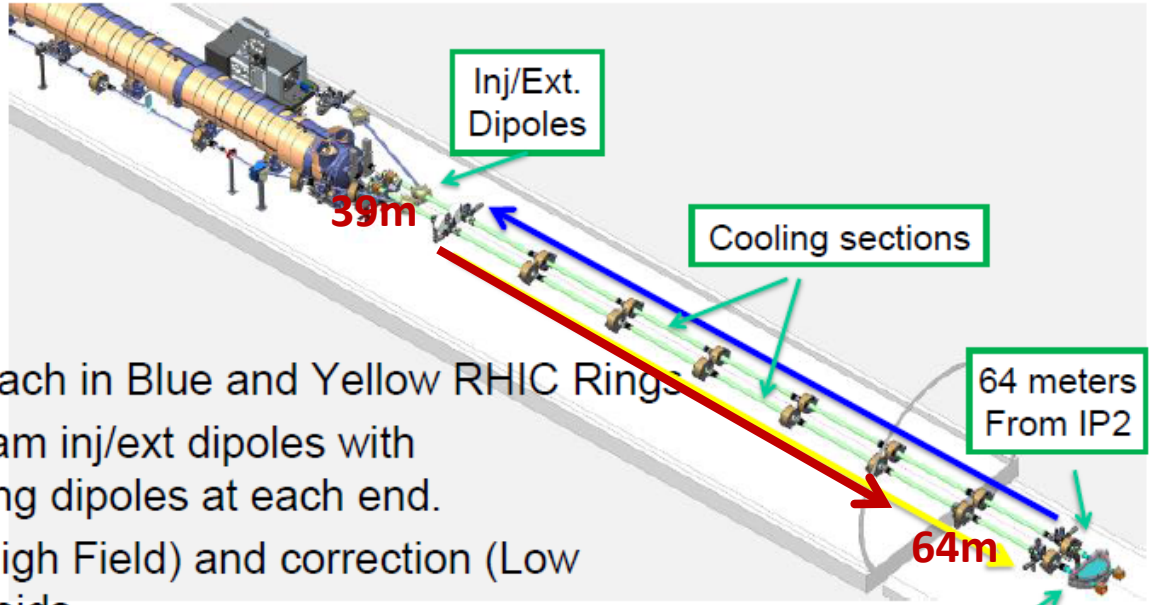

- 18 Meters each in Blue and Yellow RHIC Rings
- Electron beam inj/ext dipoles with compensating dipoles at each end.
- Matching (High Field) and correction (Low Field) solenoids.
- RHIC "warm" beam tube with NEG coating and μ metal shielding.

BROOKHAVEN NATIONAL LABORATORY

10

Office of Science U.S. DEPARTMENT OF ENERGY

May 11 2015

Courtesy A. Fedotov

Sector 1 Instrument Relocation for LEReC

May 22, 2015

Systems in the LEReC Region (39m - 64m) to be Relocated

7 separate beam line mechanical assemblies	New Location	Champions
ARTUS Kickers - Blue V, Yellow H	Sector 2	**Drees**
IPMs (Ionization Profile Monitors)- Blue H, Yellow V	Sector 12	**Tepikian**
Moveable BPM & LF Schottky, X-Y stage BI1 41m	Sector 1 (closer to Q4)	**Brown/Blaskiewicz**
BBQ Kicker stripline (1m) YO1	Sector 1 (closer to Q4)	**Marusic**
Triple Purpose Pick-Up on Moveable X-Y Stage YO1 ~42m	Sector 1 (closer to Q4)	**Minty/Marusic/Blaskiewicz**

Cable Tray Waterfall

Systems to be Removed (no longer needed)

Electron Detectors (8)	**Zhang/Blaskiewicz**
Quad Pick-up (0.25m) YO1 40.1m	**Minty**
Luminescence Monitor Cross at B02 53.1m	**Minty**
Stochastic Cooling Ceramic Pick-Ups[6-9 GHz] at BI1 67.8m	**Mernick/Brennan/Blaskiewicz**

ARTUS Kickers

- 1 Horizontal kicker and 1 Vertical kicker Assembly
- Each Assembly consists of two sets of 2 meter long strip lines
    - 7/8” and 3/8” Heliax cables
- Move to Sector 2, adjacent to existing ARTUS kickers

<u>Multi-use Striplines:</u>
Tune Meter Kickers
Longitudinal Damper
Injection Damper
Gap Cleaning

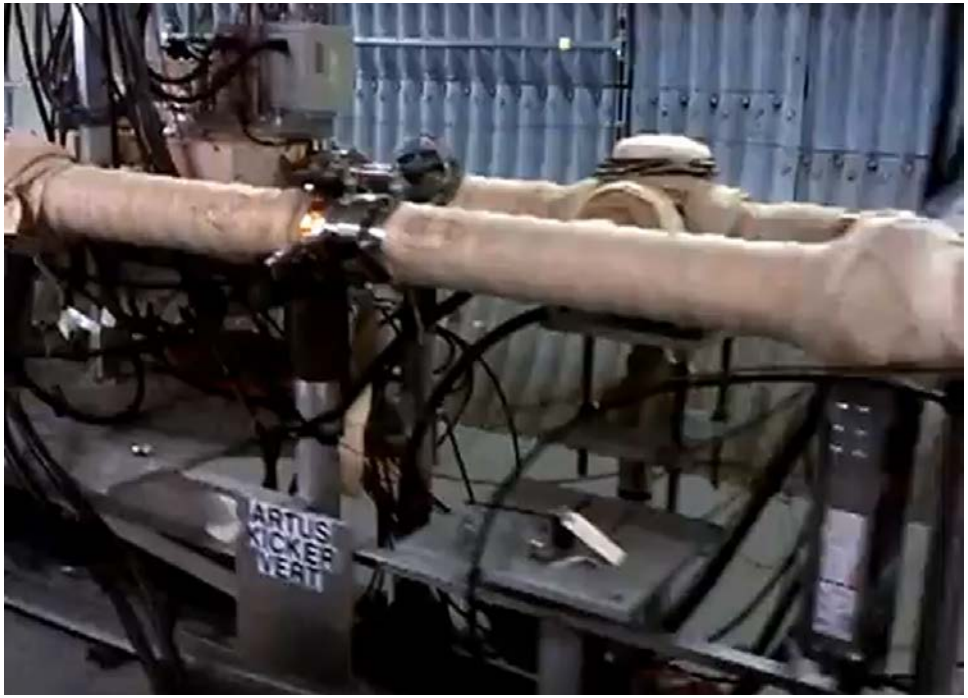

Champion: Drees

Ionization Profile Monitors

Michiko evaluated options for the IPMs:

Relocation of BH and YV IPMs:

to sector 2 ok for LEReC and 100 GeV p+p.

to sector 12 required to resolve profiles for 250 GeV p+p.

After consultation with Wolfram (03/16/15), IPMs will be relocated to sector 12.

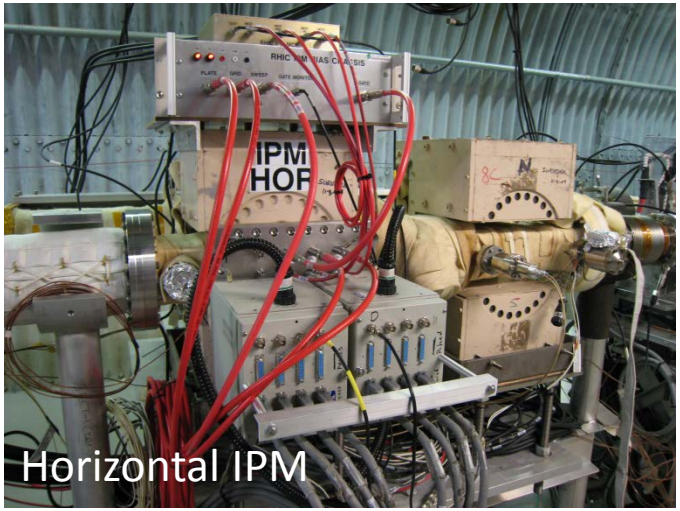

Horizontal IPM

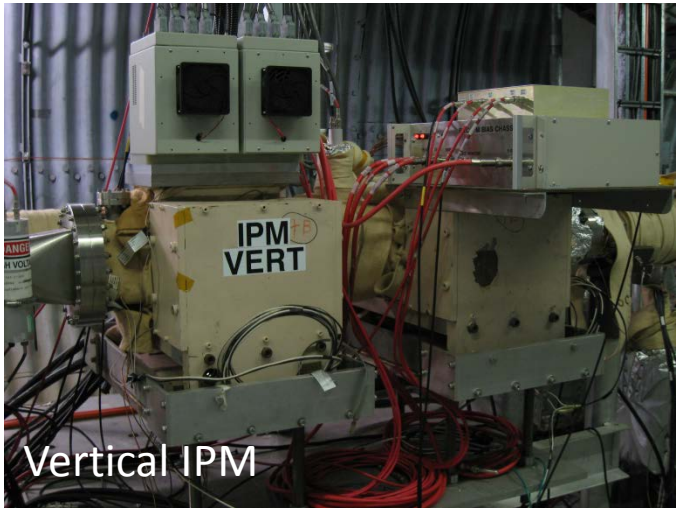

Vertical IPM

Electronics will be moved from 1002 to 1012

Each IPM has ~30 cables

A common stand for both IPMs in sector 12 was considered until Jesse found a conflict. Present plan is for separate stands with the IPMs offset enough for clearance.

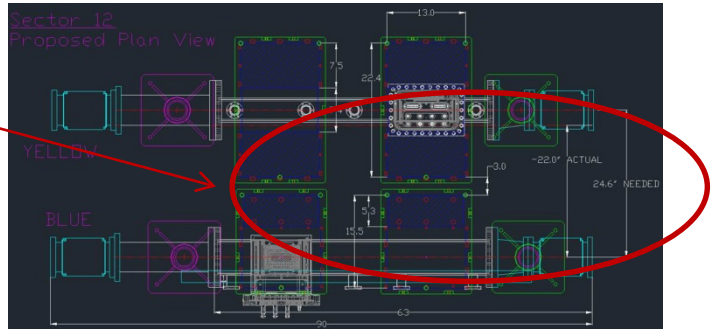

Champion: Tepikian

Moveable BPM & LF Schottky

Move from BI1 41m (from IP2) to 65m (closer to Q4)

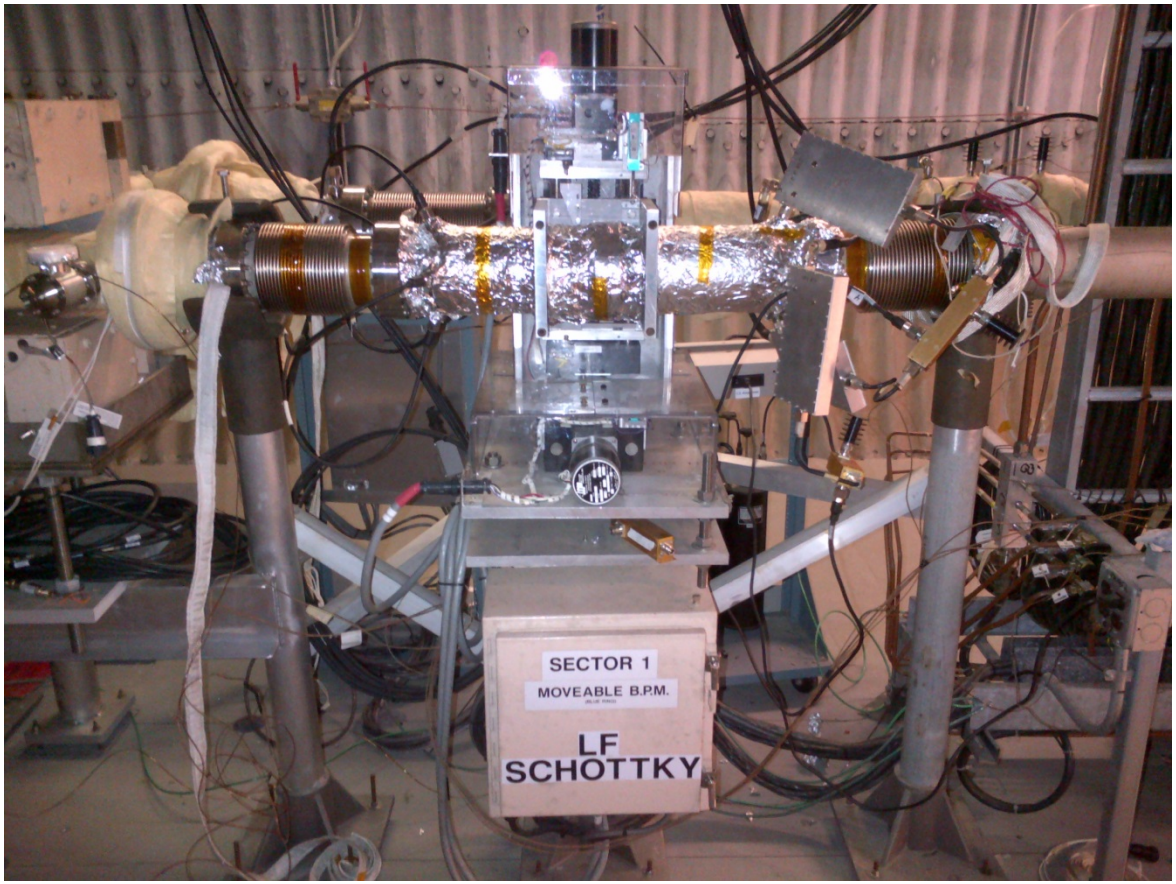

¼” heliax and motion control cables

Champions: Brown/Blaskiewicz

Triple Pick-up Assembly

Move from YO1 42m to 66m (closer to Q4)

BBQ stripline pick-up (1m)
Quad pick-up (0.25m)
Head-Tail pick-up (1m)

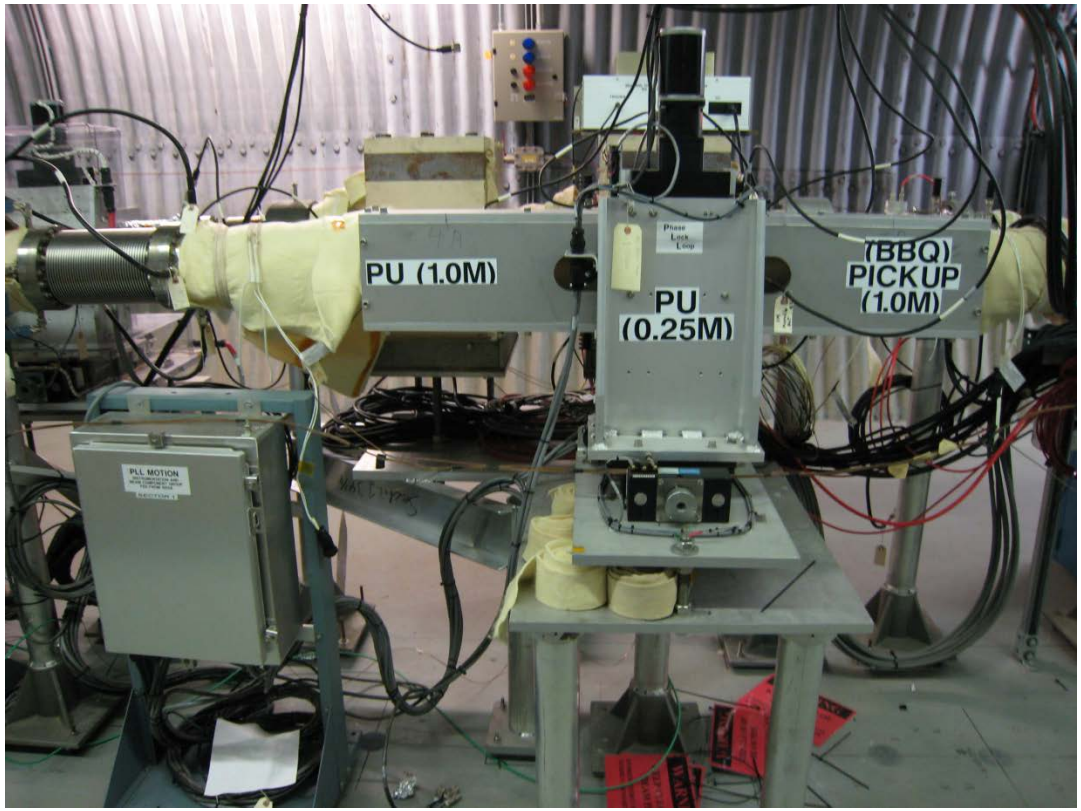

¼” heliax and motion control cables

Champions: Minty/Marusic/Blaskiewicz

BBQ Kicker (1m strip line)

Move from YO1 40m to 64m (closer to Q4)

Base-Band Tune Stripline Kicker

3/8” heliax cables

Champion: Marusic

Cable Tray Waterfall (near Q3)

Cables will be rerouted in new tray
- Power supply
- Vacuum
- Instrumentation
- Cryo

Dave Phillips working on placing two trays: one against the triplet on the inside of the ring and one against the DX inside of the ring.

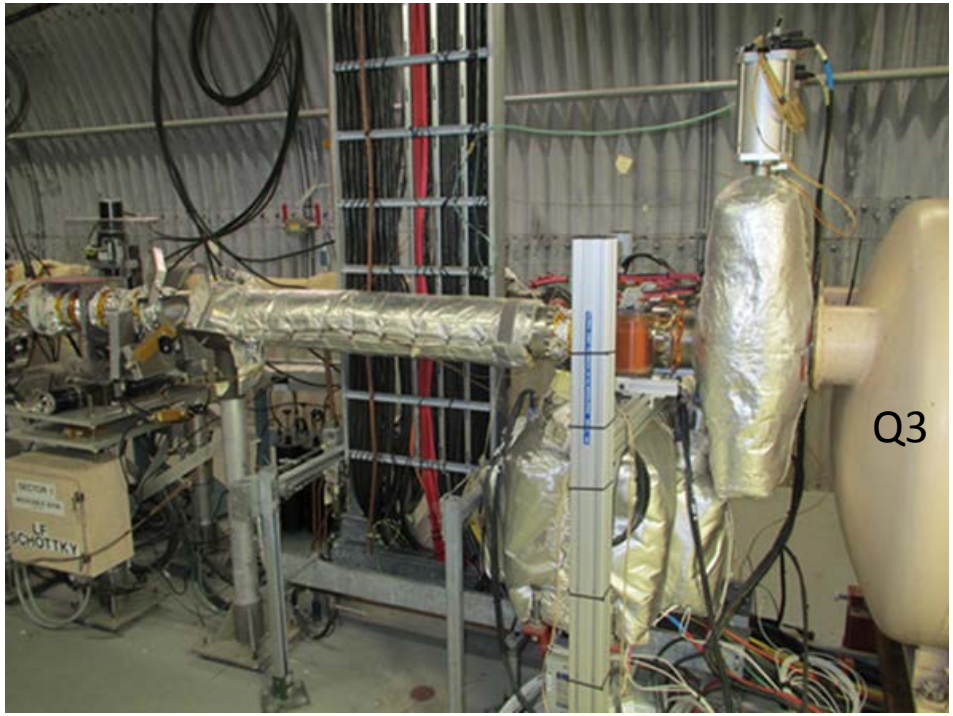

Allotment Drawings

- Sector 1 Before Relocation
- Sector 1 After Relocation

- Sector 2 Before Relocation
- Sector 2 After Relocation

- Sector 12 Before Relocation
- Sector 12 After Relocation
  - courtesy Vito De Monte

Sector 1 Before Relocation

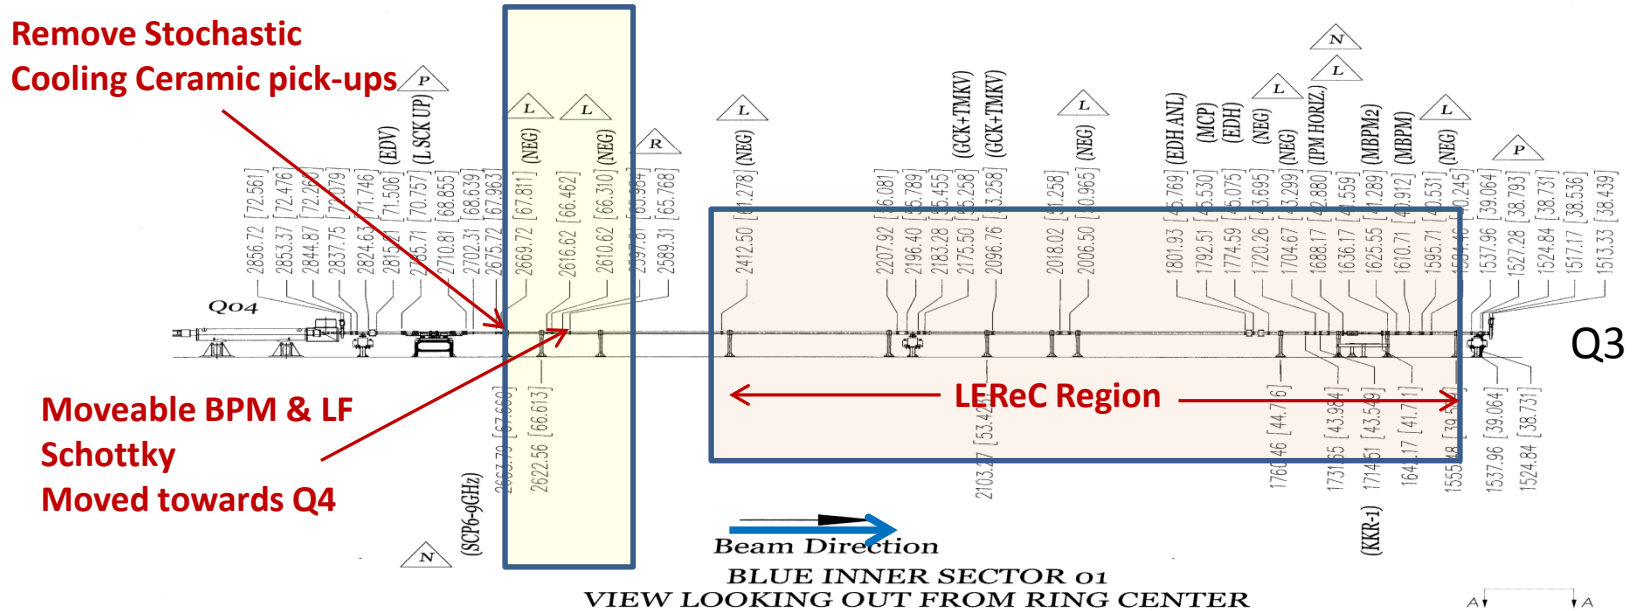

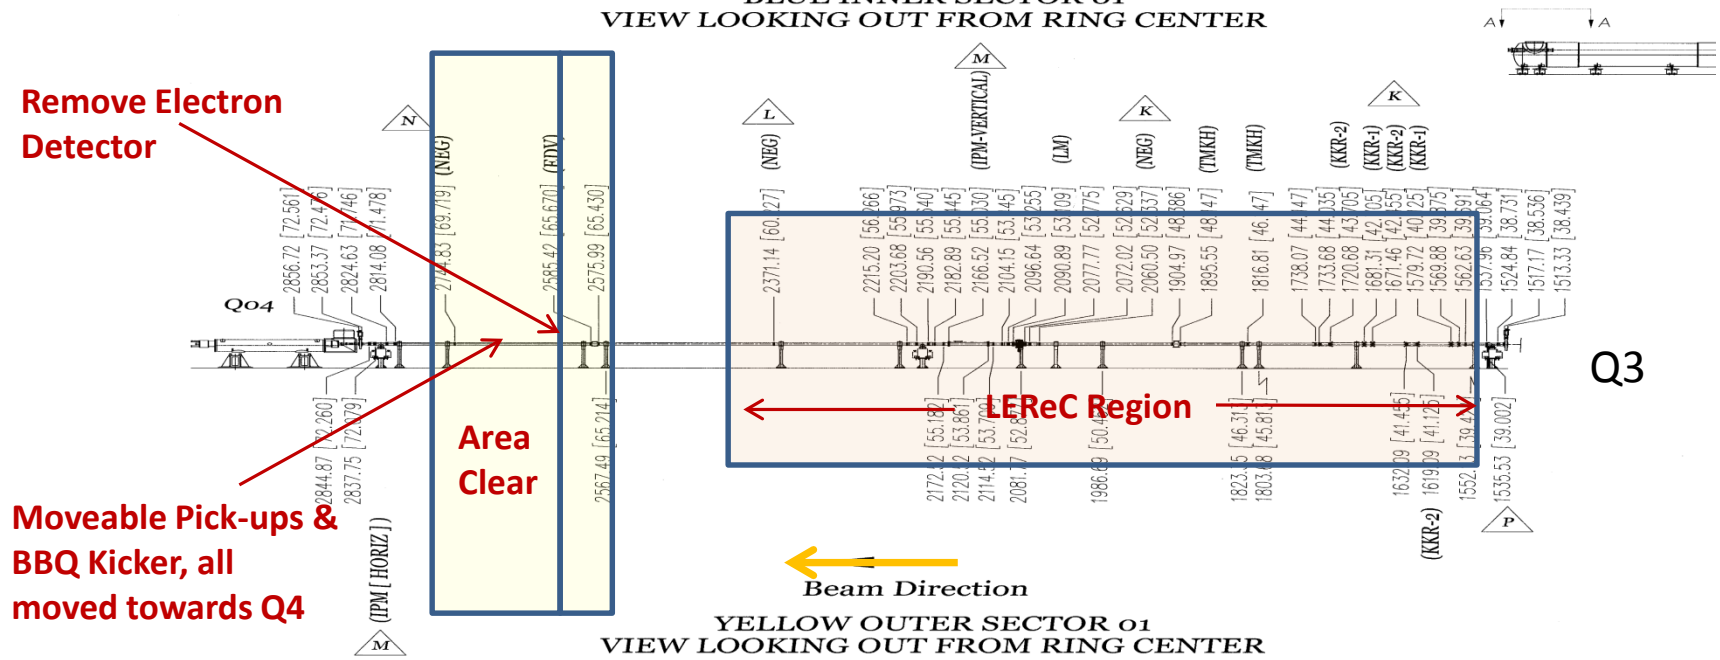

Sector 1

After

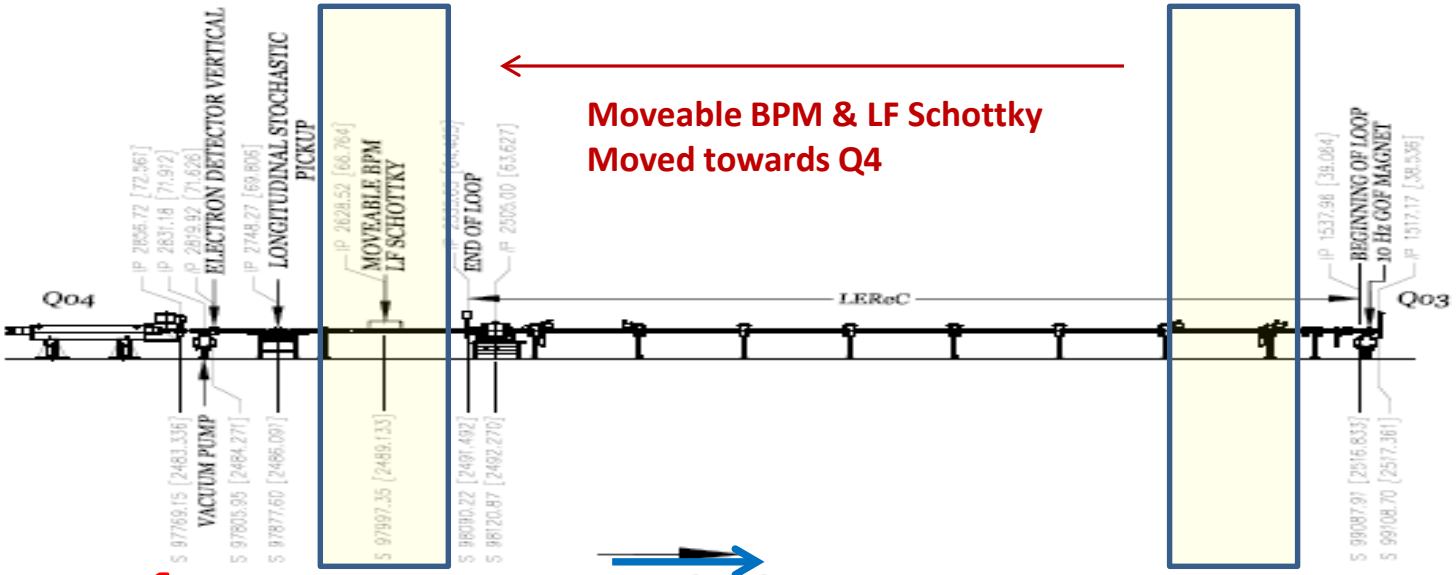

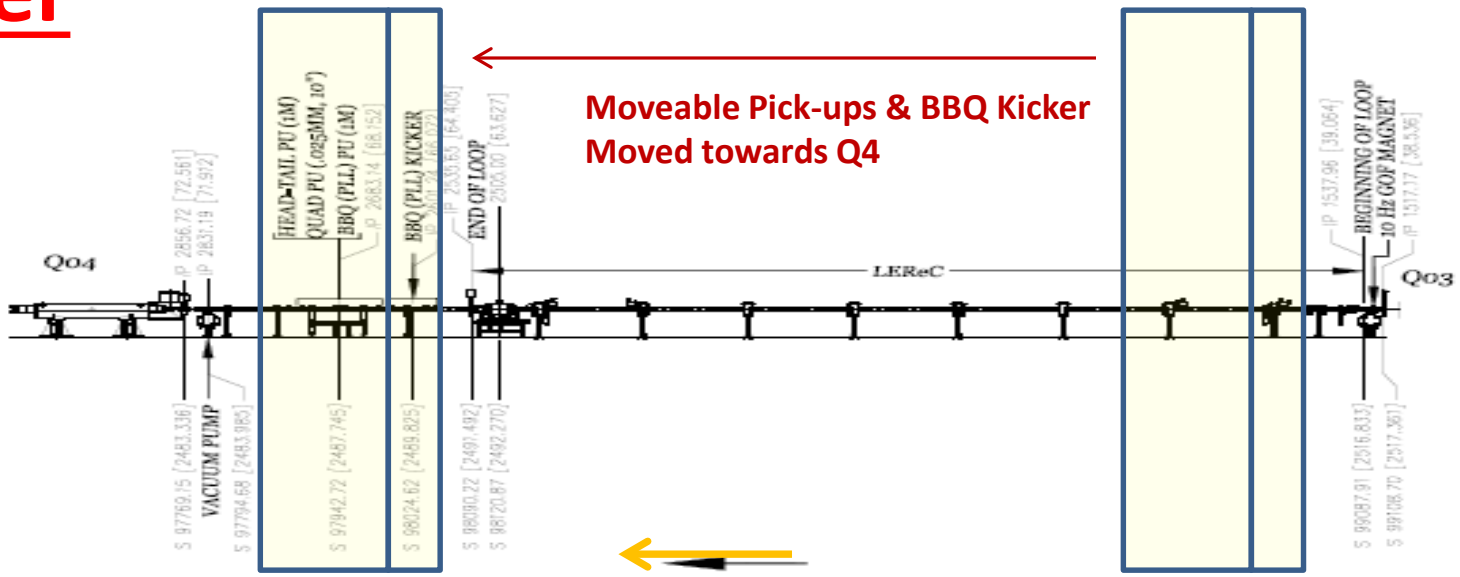

Sector 2 Before Relocation

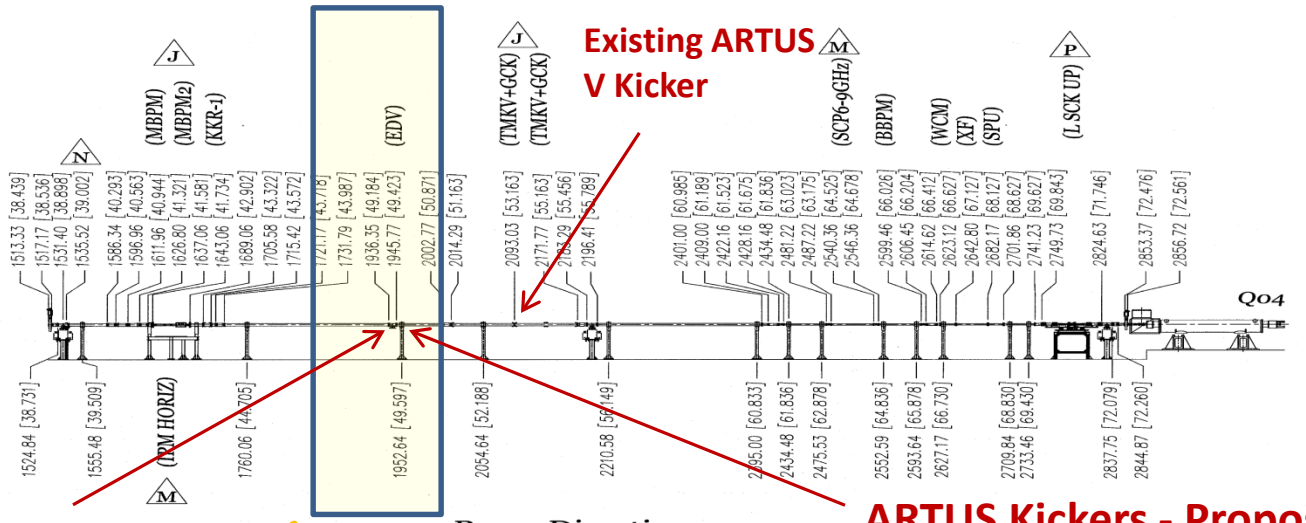

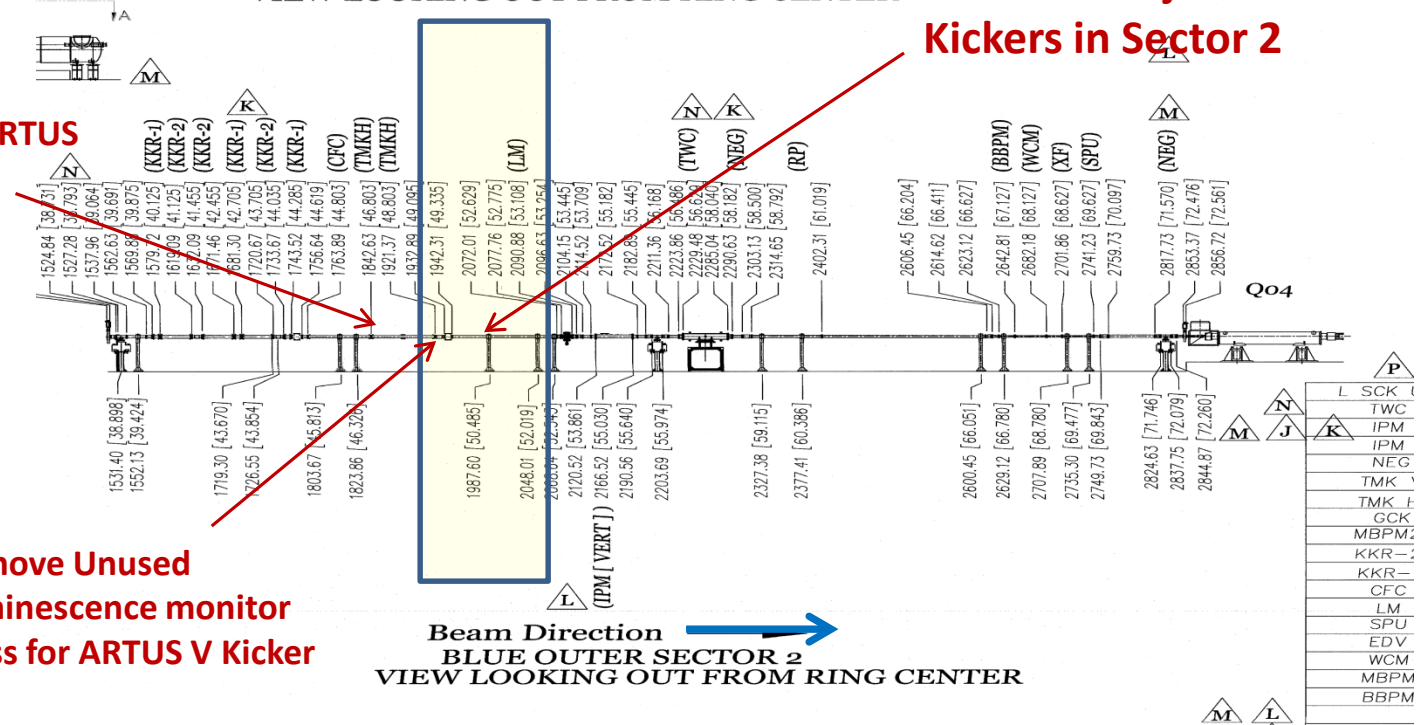

Sector 2

After

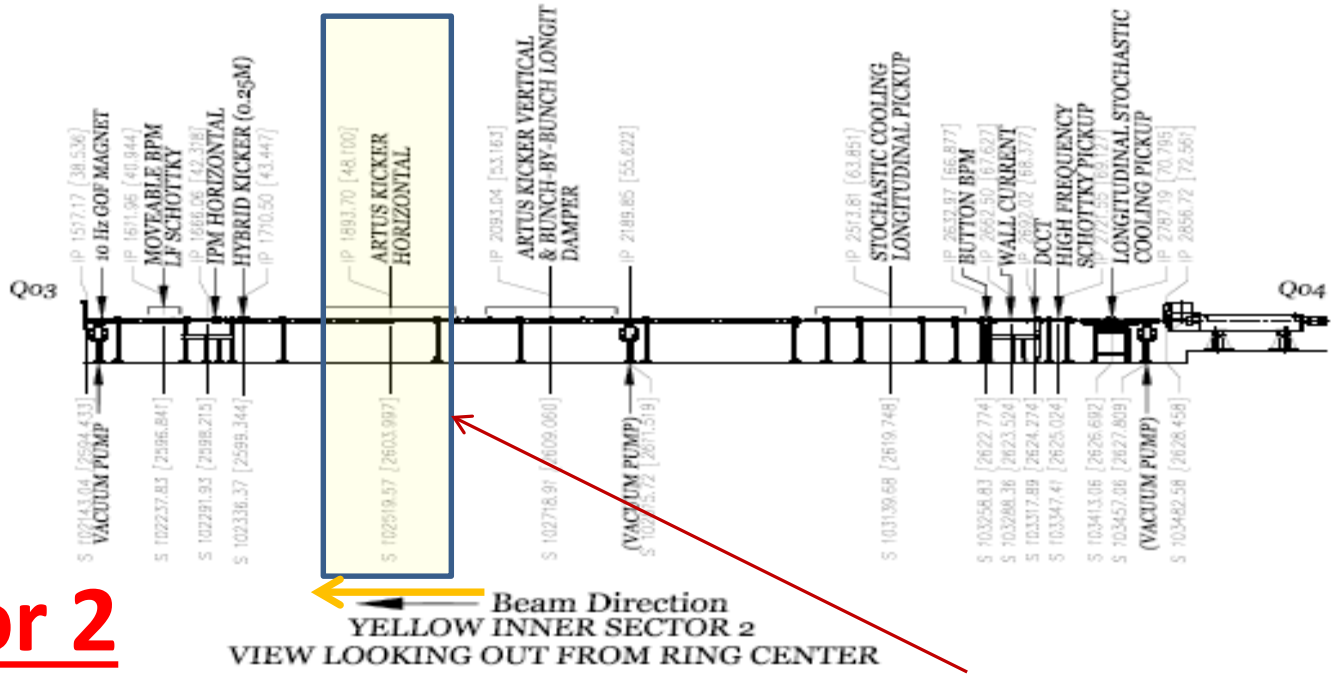

ARTUS Kickers moved from Sector 1

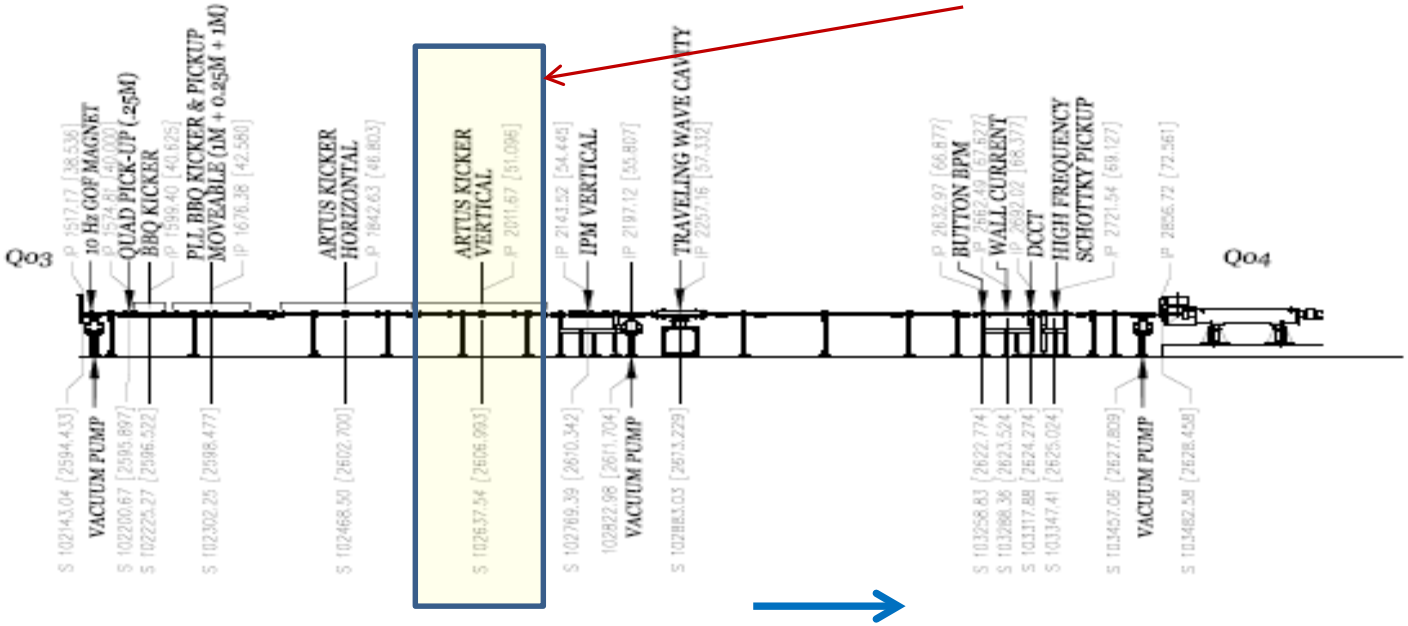

Sector 12 Before Relocation

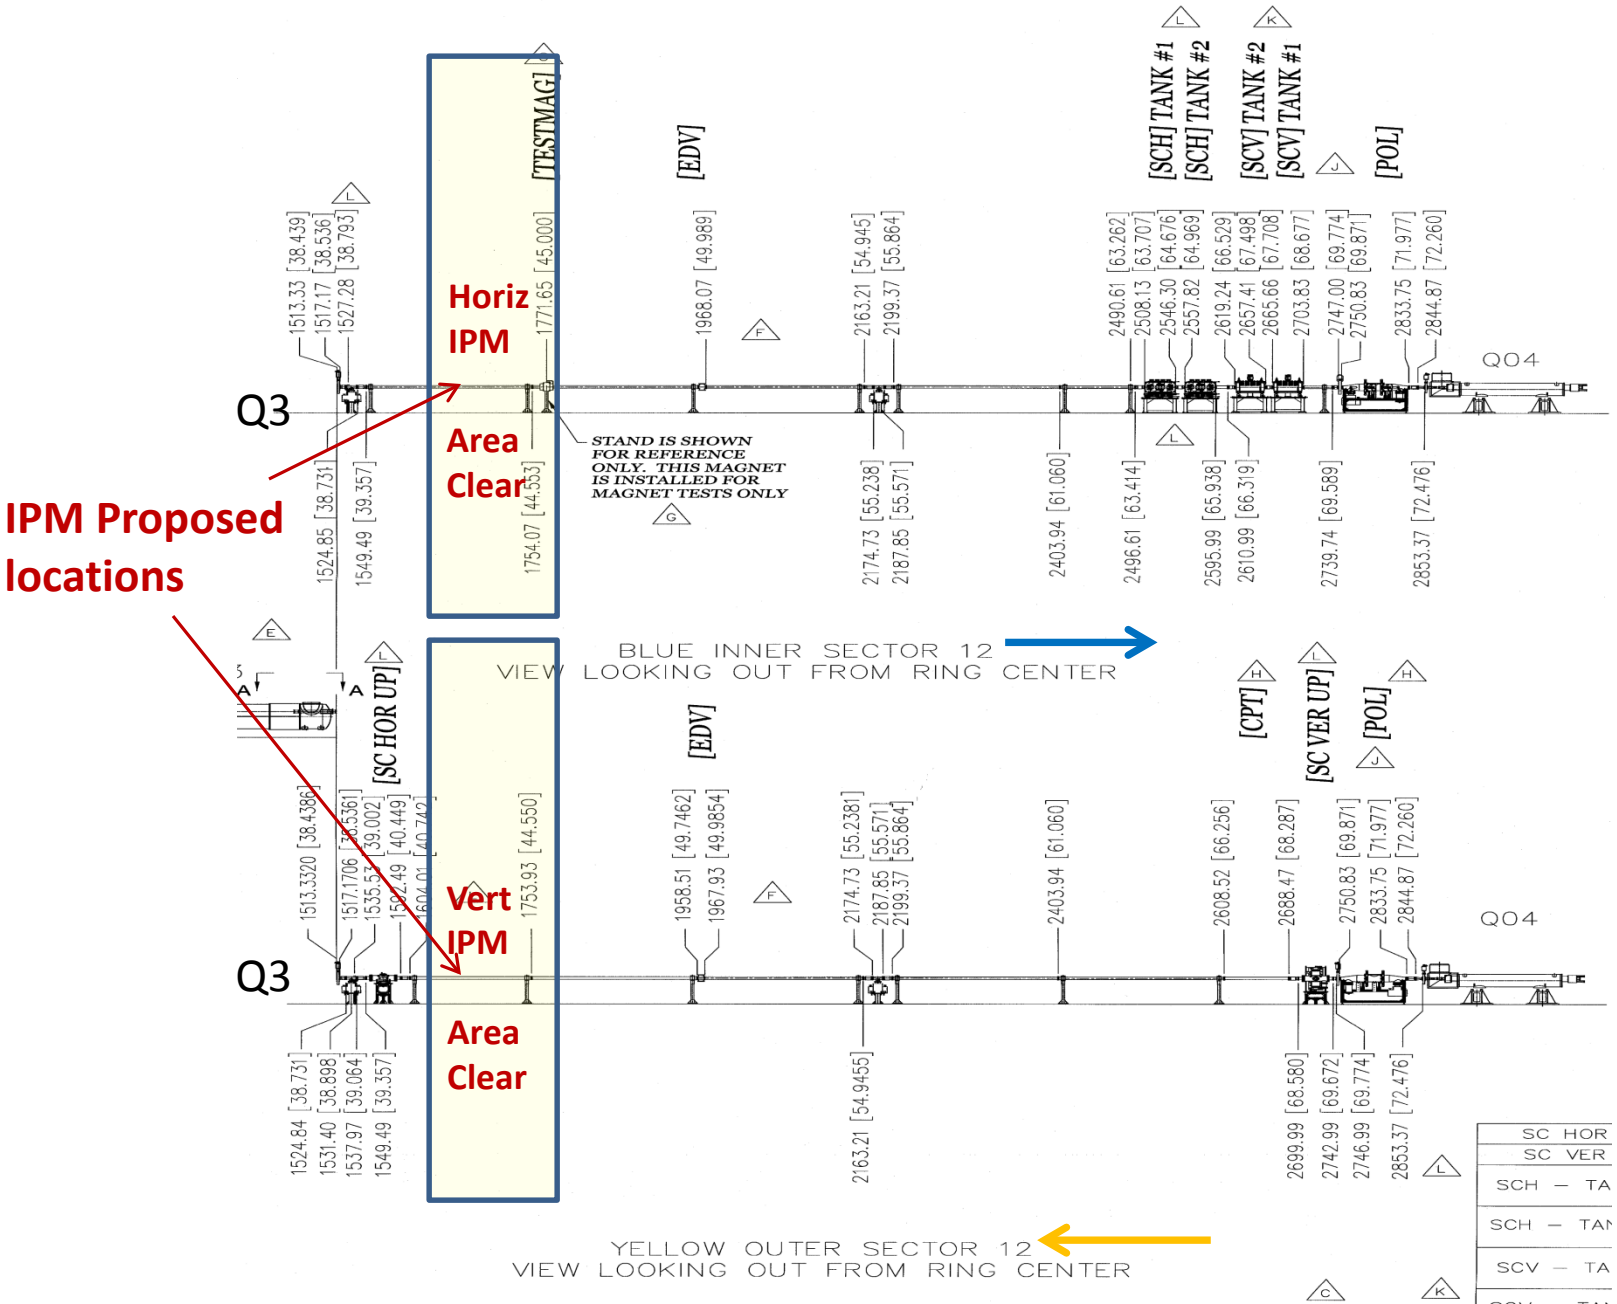

Sector 12 After

IPMs moved from Sector 1

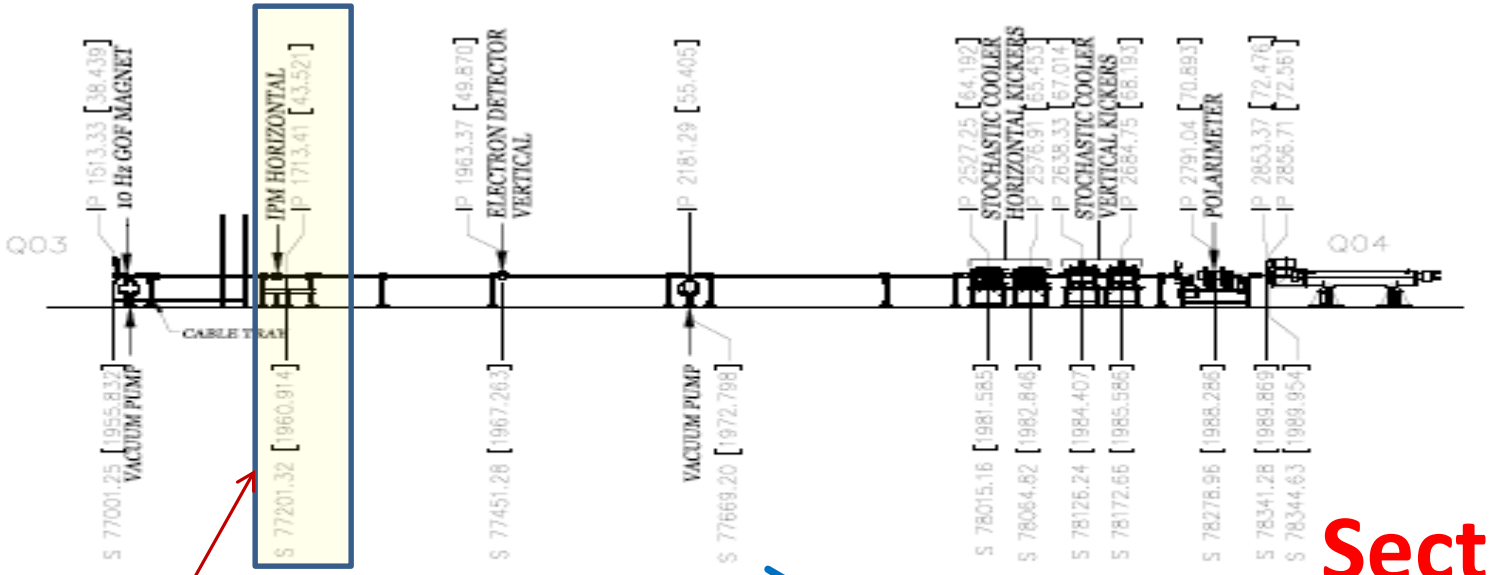

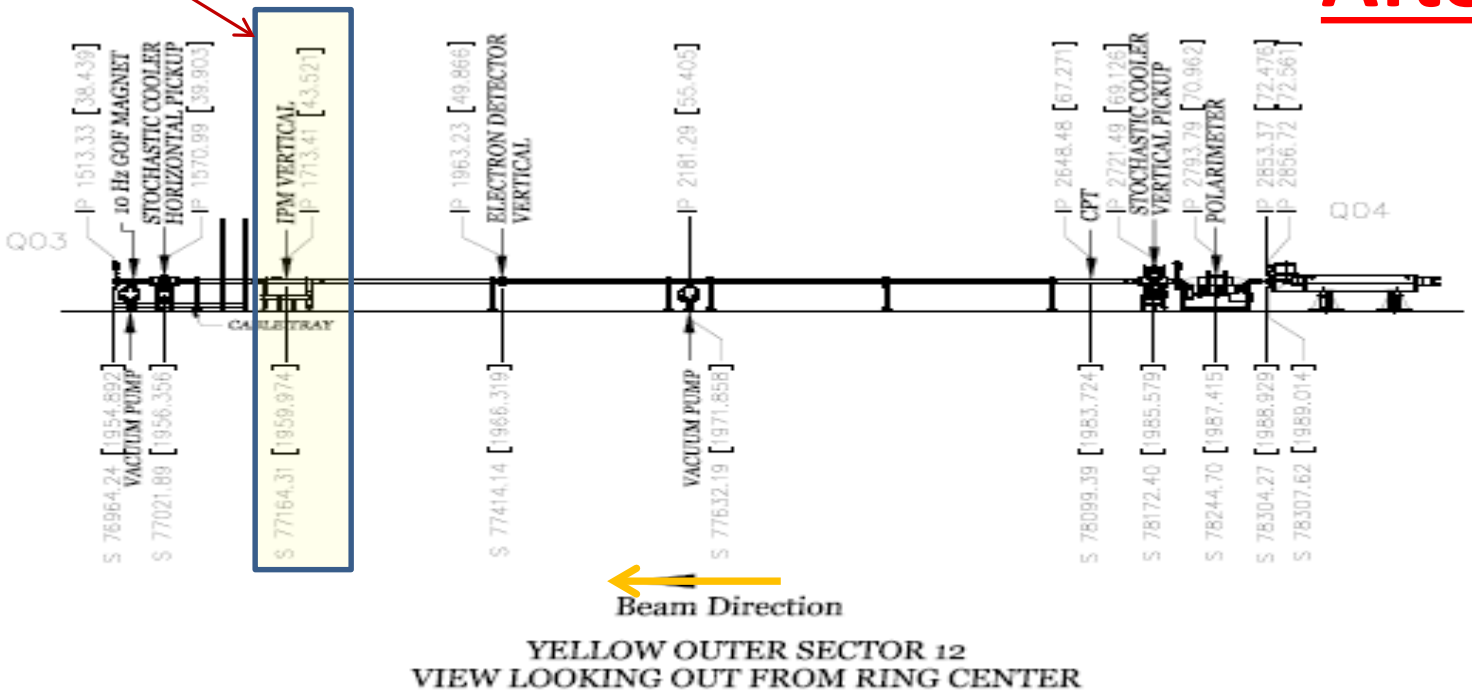

Sector 1 Instrument Relocation for LEReC

Summary

Champions need to confirm the relocation plan so the mechanical design work can proceed.

More details can be found here:
http://www.cadops.bnl.gov/Instrumentation/InstWiki/index.php/Instrumentation_Relocation

Systems in the LEReC Region (40m - 63m) to be Relocated

7 separate mechanical assemblies	New Location	Champion
ARTUS Kickers - Blue V, Yellow H	Sector 2	**Drees**
IPMs (Ionization Profile Monitors)- Blue H, Yellow V	Sector 12	**Tepikian**
Moveable BPM & LF Schottky, X-Y stage BI1 41m	Sector 1 (closer to Q4)	**Brown/Blaskiewicz**
BBQ PLL Kicker stripline (1m) YO1	Sector 1 (closer to Q4)	**Marusic**
Triple Purpose Pick-Up on Moveable X-Y Stage YO1 ~42m	Sector 1 (closer to Q4)	**Minty/Marusic/Blaskiewicz**
Cable Tray Waterfall		

Systems to be Removed

Electron Detectors (8)	**Zhang/Blaskiewicz**
Quad Pick-up (0.25m) YO1 40.1m	**Minty**
Luminescence Monitor Cross at B02 53.1m	**Minty**
Stochastic Cooling Ceramic Pick-Ups[6-9 GHz] at BI1 67.8m	**Mernick/Brennan/Blaskiewicz**

Beam Loss Monitor Detector Reconfiguration, Sector 1

1 BLM per IPM will move with the IPMs to sector 12	**Drees**

Sector 1 Before Relocation

Sector 1

YO1 S	Meters from IP2	Yellow Outer (YO1) Label	Name	Notes	BI1 S	Meters from IP2	Blue Inner (BI1) Label	Name	Notes
2517.4	38.4		Start of warm sector	Y-valve	2517.4		Y-valve	Start of warm sector	near Q3
	38.7		10 Hz GOF Magnet					10 Hz GOF Magnet	
	39.6		EDY	Will be removed if it is still installed					
2515.9	39.8	KKR-1	Quad PU (0.25m, 10")	Will be removed					
	40m		Start LEReC			40m		Start LEReC	
2515.2	40.1	KKR-2	BBQ (PLL) Kicker (1m, 39")	(twisted pr push-pull)	2515.1	40.9	MBPM	LF Schottky resonant PU (BPM)	All one moving assy
					2514.7	41.3	MBPM2	LF Schottky BPM for centering	53" length
2513.9	41.5	KKR-2	Head-Tail PU (1m)						
2513.3	42.4	KKR-1	Quad PU (0.25m, 10")	All one moving assy					
2512.6	42.7	KKR-2	BBQ (PLL) PU (1m)	115" length	2513.3	42.8	IPM H	B-Ionization PM Horiz (54")	
					2512.9	43.5	KKR-1	Hybrid Kicker (0.25m)	Not needed, will be removed
2510.7	46.1	TMKH	ARTUS Kicker Horizontal (start) 2m long		2510.5	45.5	Electron det. Y	MCP & RHIC ED Vertical	
2508.7	48.1	TMKH	ARTUS Kicker Horizontal 2m long		2510.2	45.7	EDH-ANL	Electron Detector Horizontal	Not Needed, will be removed
	48.3	EDY	Electron detector Y	Not needed					
			Pin diodes (4)						
	53.1	LM	Lumi-mon (only a cross)	Not needed	2503.6	53.2	GCK+TMKY	ARTUS Kicker Y, 2m (or Bunch-by-Bunch longit damper?)	
								This device was removed for service as of 10-21-13	
2501.8	55	IPM-Y	Y-Ionization PM Vert (58")		2501.6	55.2	GCK+TMKY	ARTUS Kicker Y, 2m (or Bunch-by-Bunch longit damper?)	
	63m		End LEReC U-Turn			63m		End LEReC U-Turn	
	64m		1 meter space needed?			64m		1 meter space needed?	
	~7 Meters of open space					~2 Meters of open space			
						66	R-SC Ceramic PU		
						68.6	R-SC PU	Existing	
						69	R-SC PU New desig	Future	
	71.5		Bellows & Vacuum pump						
2483.4	72.5		End of warm sector	Y-valve	2483.4		Y-valve	End of warm sector	near Q4

Sector 1 After Relocation

Sector 1

YO1	Meters	Yellow Outer (YO1)			BI1	Meters	Blue Inner (BI1)		
S	from IP2	Label	Name	Notes	S	from IP2	Label	Name	Notes
2517.4	38.4		Y-valve go1-sv3	Start of warm sector	2517.4	38.4	Y-valve, bi1-sv3	Start of warm sector	near Q3
	38.7		10 Hz GOF Magnet			38.7		10 Hz GOF Magnet	
2515.9					2515.9				
	40m		Start LEReC			40m		Start LEReC	
2491.9	63m		End LEReC U-Turn		2491.9	63m		End LEReC U-Turn	
2491.4			Vacuum Valve		2491.4			Vacuum Valve	
2490.4	64.3	KKR-2	BBQ (PLL) Kicker (1m, 39")	(twisted pr push-pull)	2489	64	MBPM	LF Schottky resonant PU (BPM)	All one moving assy
					2488	65	MBPM2	LF Schottky BPM for centering	53" length
2489.8	65.7	KKR-2	Head-Tail PU (1m)						
	66.6	KKR-1	Quad PU (0.25m, 10")	All one moving assy					
2487.6	66.9	KKR-2	BBQ (PLL) PU (1m)	115" length					
					2485.2	68.6	R-SC PU		Existing
						69	R-SC PU New desig	Future reserved space	
2484	71.5		Vacuum pump		2484	71.5		Vacuum pump	
2483.4	72.5		Y-valve, go1-sv4	End of warm sector	2483.4	72.5	Y-valve, bi1-sv4	End of warm sector	near Q4

Sector 2 Before Relocation

Sector 2

YI2 S	Meters from IP2	Yellow Inner Label	Name	Notes	BO2 S	Meters from IP2	Blue Outer Label	Name	Notes
2594.4	38.4		Start of warm sector		2594.4			Start of warm sector	near Q3
			10 Hz GOF Magnet					10 Hz GOF Magnet	
		MBPM	Moveable BPM			40.12	KKR-1	Quad Pick-up (0.25m)	
2596.5		MBPM2	Moveable BPM (LF Schottky)		2596.5	41.12	KKR-2	BBQ Kicker (1m)	
2598	41.5	IPM-H	Y-Ionization PM horizontal						
			Beam Loss Monitor		2598.5	42.9	KKR-2	PLL BBQ PU -Head-tail (1m) Moveable	
2599.3	42	KKR-2	Hybrid Kicker (0.25m)				KKR-1	Pick-up (0.25m) Moveable	
							KKR-2	Baseband PLL Kicker (1m) Moveable	
					2601	43.5	TMKH	ARTUS Kicker Horizontal (start)	
	~7 Meters of open space				2603	46.1	TMKH	ARTUS Kicker Horizontal (end)	
					2604.1	48.3	EDY	Electron Det Y	To be removed
2605.1	47.8	EDY	Electron Det Y	To be removed					
						~4 Meters open space			
2608	53	TMKY	ARTUS Kicker Y(or Bunch-by-Bunch longit damper)		2608.8	53	LM & EDY	Lumi-Mon & EDY (6-way cross)	Will remove
2610	55	TMKY	ARTUS Kicker Y(or Bunch-by-Bunch longit damper)		2610	55	IPM-Y	B-Ionization PM Vertical	
2611	56		Vacuum pump	not moved	2611			Vacuum pump	
					2612	58	TWC	Traveling Wave Cavity	
	~5 Meters of open space					~7 Meters of open space			
2617.4	61.8	SC Long Pick-up (start)							
	64	SC Long Pick-up (middle)							
	66	SC Long Pick-up (end)							
	67	Button BPM			2622	67	Button BPM		
2623	68	WCM			2623.5	68	WCM		
2614.3	68.6	DCCT			2624.3	68.6	DCCT		
	69	HF Schottky PU				69	HF Schottky PU		
		Pin diodes (2)							
	71	New Long SC pickup							
2628.4			Y-valve, End of warm sector		2628.4			End of warm sector	near Q4

Sector 2 After Relocation

Sector 2

YI2	Meters	Yellow Inner			BO2	Meters	Blue Outer		
S	from IP2	Label	Name	Notes	S	from IP2	Label	Name	Notes
2594.4	38.4		v-valve, gi2-sv3	near Q3	2594.4	38.4		v-valve, bo2-sv3	near Q3
			10 Hz GOF Magnet	not moved				10 Hz GOF Magnet	not moved
		MBPM	Moveable BPM			40.12	KKR-1	Quad Pick-up (0.25m)	not moved
		MBPM2	Moveable BPM (LF Schottky)	not moved	2596.5	41.12	KKR-2	BBQ Kicker (1m)	not moved
2598	41.5	IPM-H	Y-Ionization PM horizontal	not moved	2598.5	42.9	KKR-2	PLL BBQ PU (1m) Moveable)	not moved
			Beam Loss Monitor	not moved			KKR-1	Pick-up (0.25m) Moveable	not moved
2599.3	42	KKR-2	Hybrid Kicker (0.25m)				KKR-2	Baseband PLL Kicker (1m) Move	not moved
2600.8	43.5	TMKH	ARTUS Kicker Horizontal (start) 2m long		2601	43.5	TMKH	ARTUS Kicker Horizontal (start)	not moved
2603.4	46.1	TMKH	ARTUS Kicker Horizontal 2m long		2603	46.1	TMKH	ARTUS Kicker Horizontal (end)	not moved
					2605	50	GCK+TMKV	ARTUS Kicker V, 2m (Bunch-by-Bunch longit damper)	
					2609	54	GCK+TMKV	ARTUS Kicker V, 2m (Bunch-by-Bunch longit damper)	
2608	53	TMKV	ARTUS Kicker V(or Bunch-by-Bunch	not moved					
2610	55	TMKV	ARTUS Kicker V(or Bunch-by-Bunch	not moved	2610	55	IPM-V	B-Ionization PM Vertical	not moved
2611	56		Vacuum pump	not moved	2611	56		Vacuum pump	not moved
					2612	58	TWC	Traveling Wave Cavity	not moved
	~5 Meters of open space					~7 Meters of open space			
2617.4	61.8	SC Long Pick-up (start)		not moved					
	64	SC Long Pick-up (middle)		not moved					
	66	SC Long Pick-up (end)		not moved					
2622	67	Button BPM		not moved	2622	67	Button BPM		not moved
2623	68	WCM		not moved	2623.5	68	WCM		not moved
2624.3	68.6	DCCT		not moved	2624.3	68.6	DCCT		not moved
2624.8	69	HF Schottky PU		not moved	2624.8	69	HF Schottky PU		not moved
		Pin diodes (2)		not moved					
	71	New Long SC pickup		not moved					
			Vacuum Pump	not moved				Vacuum Pump	not moved
2628.4			V-valve, gi2-sv4	near Q4	2628.4			V=valve, bo2-sv4	near Q4
