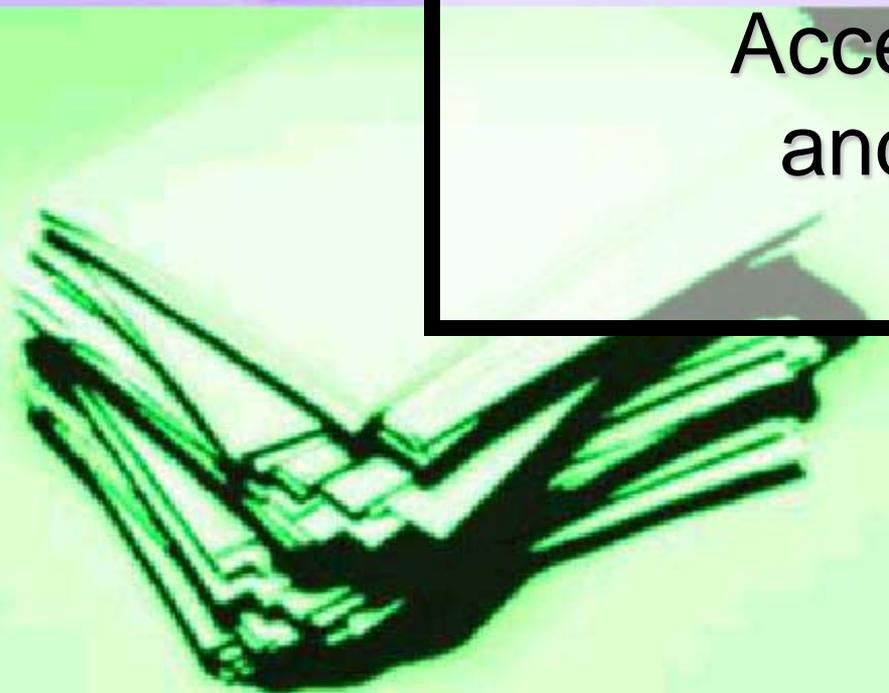


A stack of white papers, slightly blurred, set against a light blue background.A blurred image of a clock face, showing numbers and hands, set against a light purple background.

Run 2016

A stack of white papers, slightly blurred, set against a light green background.A clear image of a yellow clock face with black numbers and hands, set against a yellow background.

**Accelerator Support
and Maintenance**

Run 16



RHIC Maintenance

- Injectors:
- LINAC and Booster Remain on for NSRL and BLIP
- RHIC:
 - Sector 2 CeC cathode install
 - Experimental access
 - Maintenance items

RHIC Maintenance Wed 4/18 0700-1000hrs

Time	Activity	Group
0600hrs	AGS off, Begin MG set maintenance. NOTE: Booster and LINAC on for NSRL and BLIP	MCR
0800hrs	RHIC Maintenance begins: RHIC Sector Valves Closed. RA Sectors 2 & 4. WXY RA CA sector 12 XA sectors 6, 8 & 10 (HP Surveys before CA 9z1or10z2)	VAC MCR/MSG MCR/MSG MCR/MSG
1200hrs	Sweep/Secure sector 4, RFNA after, sweep WXY	CAS/MCR
1400hrs	Sweep secure sectors 10, sector 2 tunnel (IR remains opened) Begin RPS recovery	CAS/MCR
1530hrs	Sweep STAR, PHENIX, IR2	CAS/MCR
1600hrs	Hysteresis ramp after IR2 secure	RPSG/MCR
1630hrs	Physics restoration	AP/MCR
